



BAKERSFIELD FREEWAY CONNECTOR | LOOKING NORTH AT THE STATE ROUTE 58 AND 99 INTERCHANGE WHERE CONSTRUCTION EXTENDS THE 58 FREEWAY WEST AND BUILDS NEW RAMP CONNECTORS AND IMPROVES EXSTING RAMPS

## Kern Council of Governments

# Progress Report for Projects of Regional Significance

**APRIL 2024 EDITION**

**This report is updated quarterly  
and posted on the Kern COG  
website at [www.kerncog.org](http://www.kerncog.org)**



**Kern Council  
of Governments**

## What's Inside?

Status Information on:

Safety & Maintenance — Page 1

Projects throughout County— Page 9

Metro. Bakersfield Projects— Page 11

Completed Projects— Page 13



**THANK YOU**  
*to our Caltrans and local  
project managers and  
planning staff who  
contribute to this report.*

Questions or comments? Please contact:

Rochelle Invina-Jayasiri  
[rinvina@kerncog.org](mailto:rinvina@kerncog.org)

# PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

## Countywide - Highway Safety and Maintenance

SR 58 - PM 91.8/91.8 - Near Tehachapi - construct new maintenance station




**PROJECT COST:** \$16,783,000      Cost estimates are subject to revision.

- ENV**    100%    *Completed June 2020*
- DES**    100%    *Completed June 2022*
- ROW**    100%    *Completed June 2022*
- CON**    50%    *Expected completion Summer 2024*

KERSHOPP20003 - 09-36750 - Project Manager: Jeremy Milos

SR 119 - PM 28.2/31.3 - Near Bakersfield Ashe Rd to SR 99 - rehabilitate roadway, improve ramp intersections, bicycle lanes, shoulders, median lane, sideways and other ADA improvements

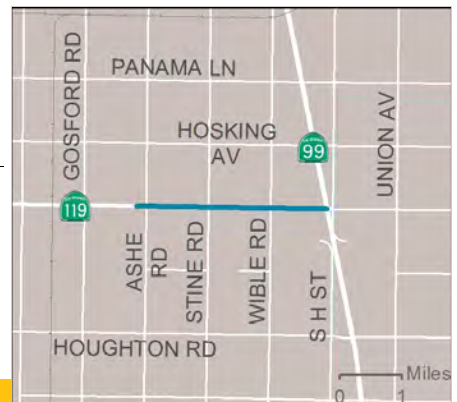


**PROJECT COST:** \$59,000,000      Cost estimates are subject to revision.

- ENV**    100%    *Completed June 2021*
- DES**    90%    *Expected completion date May 2024*
- ROW**    64%    *Expected completion date September 2024*
- CON**    0%    *Expected start date October 2024*

KERSHOPP2224 - 06-0V610 - Project Manager: Manuel Ornelas

SR 14 - PM R12.6/16.7 - Rosamond and Mojave Area - between Silver Queen Road and Business Route 58 - rehabilitate roadway and other safety improvements

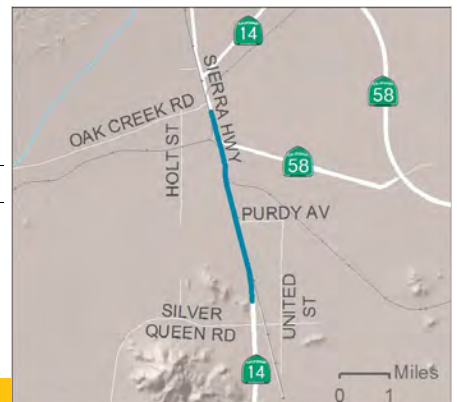


**PROJECT COST:** \$47,588      Cost estimates are subject to revision.

- ENV**    100%    *Completed June 2023*
- DES**    15%    *Start date September 2023*
- ROW**    0%    *Expected start date September 2023*
- CON**    0%    *Expected start date July 2026*

KERSHOPP2202 - 09-37520 - Project Manager: Jeremy Milos

SR 155 - PM R0.04/R1.3 - In Delano Fremont St to Browning Rd - rehabilitate roadway and other safety improvements

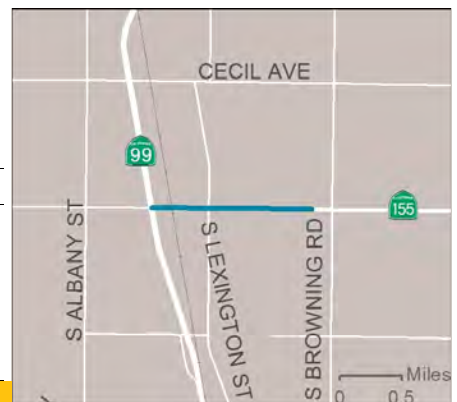

**PROJECT COST:** \$16,700,000      Cost estimates are subject to revision.


- ENV**    100%    *Completed July 2021*
- DES**    95%    *Expected completion date June 2024*
- ROW**    25%    *Expected completion date June 2024*
- CON**    0%    *Expected start date December 2024*

KERSHOPP2215 - 06-0W810 - Project Manager: Shavonne Conley

# PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

## Countywide - Highway Safety and Maintenance

SR 166 - PM 17.3/17.7 - about 7 miles west of Mettler from 0.1 miles west to 0.2 miles east of California Aqueduct. - Bridge Replacement.

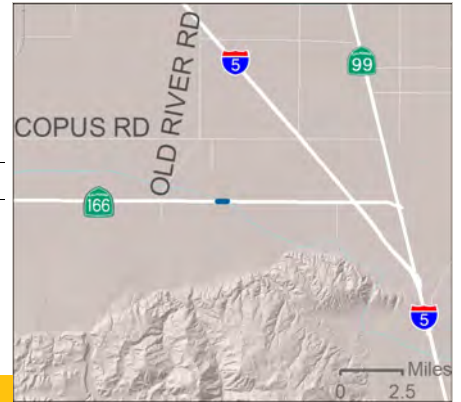


**PROJECT COST:** \$8,000,000 Cost estimates are subject to revision.

- ENV** 100% *Completed August 2022*
- DES** 100% *Expected completion by March 2024*
- ROW** 100% *Completed June 2023*
- CON** 0% *Expected start date by June 2025*

KERSHOPP1809 - 06-0S050 - Project Manager: Scott Friesen

SR 166 - PM 0.0/9.0 - In and near Maricopa SR 33 to Basic School Rd - rehabilitate roadway and culverts, upgrade guardrails, add rumblestrips, and other safety improvements

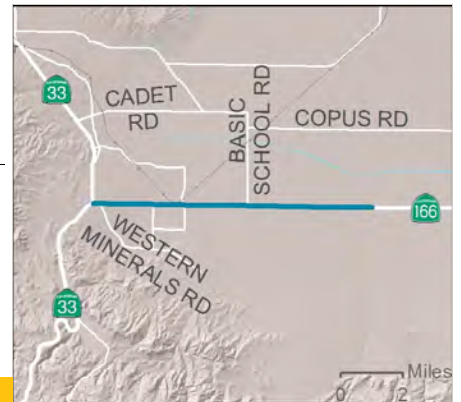


**PROJECT COST:** \$15,900,000 Cost estimates are subject to revision.

- ENV** 100% *Completed August 2022*
- DES** 100% *Completed June 2023*
- ROW** 100% *Completed May 2023*
- CON** 0% *Expected start date March 2024*

KERSHOPP2221 - 06-0X380 - Project Manager: Shavonne Conley

SR 178 - Near Ridgecrest - SR 14 to San Bernardino County - pavement rehabilitation and other improvements - long lead project

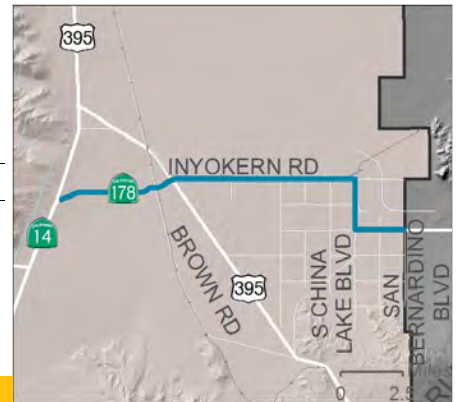


**PROJECT COST:** \$76,600,000 Cost estimates are subject to revision.

- ENV** 90% *Expected completion date June 2024*
- DES** 0% *Expected start date May 2024*
- ROW** 0% *Expected start date May 2024*
- CON** 0% *Expected start date July 2027*

KERSHOPP2201 - 09-38330 - Project Manager: Jeremy Milos

SR 184 - PM 0.8/8.6 - Near Bakersfield Dunsmere St to Breckenridge Rd - ADA curb ramps, bike lanes, pavement rehabilitation, bus turnouts, pedestrian crossings

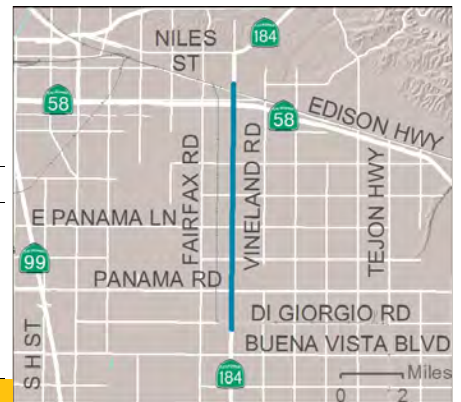

**PROJECT COST:** \$35,700,000 Cost estimates are subject to revision.

- ENV** 100% *Completed June 2021*
- DES** 90% *Expected completion November 2024*
- ROW** 75% *Expected completion November 2024*
- CON** 0% *Expected start date March 2024*


KERSHOPP2225 - 06-0U290 - Project Manager: Paul Pineda



# PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

## Countywide - Highway Safety and Maintenance

SR 223 - PM 1.85/10.4 - Interstate 5 to Costajo Road - rehabilitate roadway, upgrade guardrails and install rumblestrips

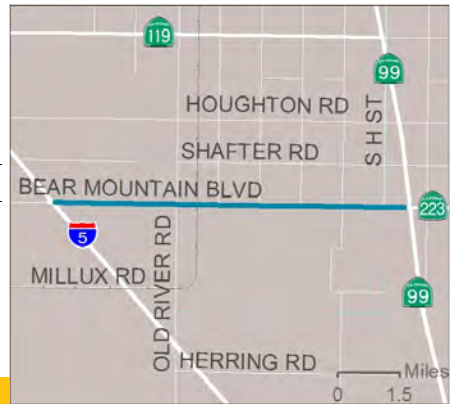


**PROJECT COST:** \$12,800,000      Cost estimates are subject to revision.

- ENV**    50%    *Expected completion date April 2024*
- DES**    0%    *Expected start date April 2024*
- ROW**    0%    *Expected start date April 2024*
- CON**    0%    *Expected start date October 2025*

KERSHOPP2207 - 06-1C060 - Project Manager: Shavonne Conley

SR 223 - PM 20.1/21.3 - In and near Arvin - Comanche Drive to St. Thomas Street - rehabilitate roadway and other safety improvements

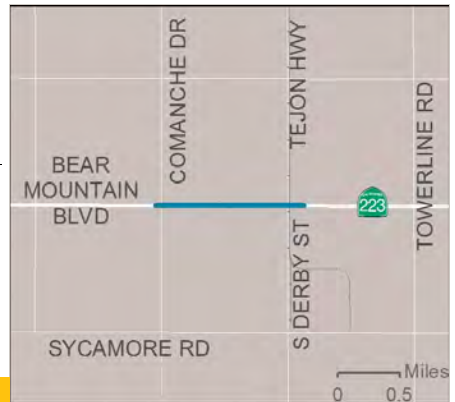


**PROJECT COST:** \$6,500,000      Cost estimates are subject to revision.

- ENV**    50%    *Expected completion Spring 2024*
- DES**    0%    *Expected start date May 2024*
- ROW**    0%    *Expected start date May 2024*
- CON**    0%    *Expected start date December 2025*

KERSHOPP2209 - 06-0Y150 - Project Manager: Marlo Carlos

SR 33 - PM 14.4/17.9 - In and near Taft - Cadet Road to south of Main Street - rehabilitate roadway and other improvements

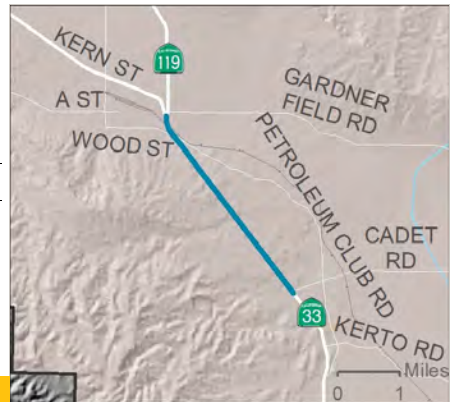

**PROJECT COST:** \$26,500,000      Cost estimates are subject to revision.

- ENV**    75%    *Expected completion date October 2024*
- DES**    0%    *Expected start date July 2024*
- ROW**    0%    *Expected start date July 2024*
- CON**    0%    *Expected start date July 2025*

KERSHOPP2205 - 06-0W830 - Project Manager: Paul Pineda

SR 33 - PM 21.8/39.8 - Near Taft Henry Rd to Cimric Rd - at various locations rehabilitate drainage systems



**PROJECT COST:** \$13,800,000      Cost estimates are subject to revision.


- ENV**    100%    *Completed June 2021*
- DES**    90%    *Expected completion date June 2024*
- ROW**    90%    *Expected completion date June 2024*
- CON**    0%    *Expected start date January 2025*

KERSHOPP2223 - 06-0X240 - Project Manager: Victor Aldama

## PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

### Countywide - Highway Safety and Maintenance

SR 33 - PM 40.4/59 - Near McKittrick Lokern Rd to SR 46 - rehabilitate roadway and other safety improvements

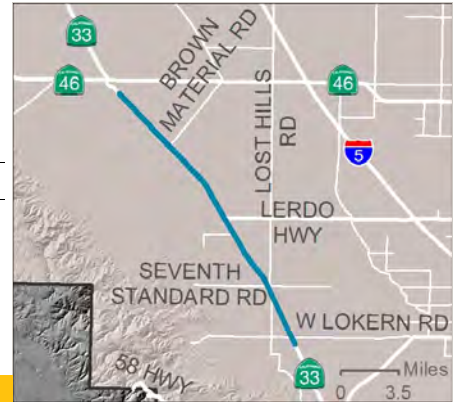


**PROJECT COST:** \$37,400,000 Cost estimates are subject to revision.

**ENV** 100% *Completed July 2022*  
**DES** 100% *Completed December 2023*  
**ROW** 100% *Completed October 2023*  
**CON** 0% *Expected start date August 2024*

KERSHOPP2218 - 06-0Y130 - Project Manager: Victor Aldama

SR 43 - PM 25.19/25.19 - In Wasco at SR 46 and Gromer Ave - construct roundabout

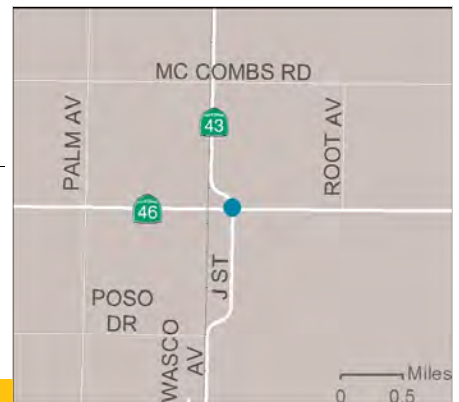


**PROJECT COST:** \$10,100,000 Cost estimates are subject to revision.

**ENV** 100% *Completed June 2021*  
**DES** 95% *Expected completion June 2024*  
**ROW** 75% *Expected completion June 2024*  
**CON** 0% *Expected start date February 2025*

KERSHOPP2220 - 06-0X770 - Project Manager: Shelley Maggard

SR 43 - PM 15.83/15.83 - In Shafter at Santa Fe Road and Los Angeles St - construct roundabout

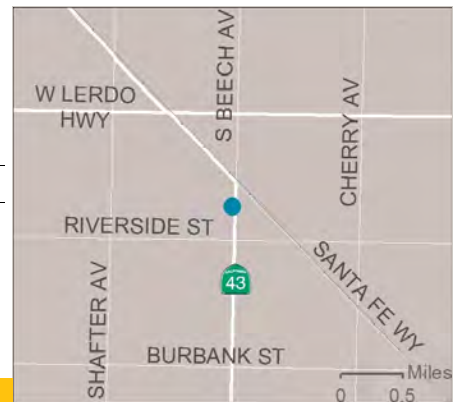


**PROJECT COST:** \$14,800,000 Cost estimates are subject to revision.

**ENV** 100% *Completed October 2022*  
**DES** 70% *Expected completion date July 2025*  
**ROW** 20% *Expected completion date July 2025*  
**CON** 0% *Expected start date January 2026*

KERSHOPP2214 - 06-1A470 - Project Manager: Victor Aldama

SR 46 - PM 51.25/57.78 - Near Wasco and Famosa - east of SR 43 to SR 99 - rehabilitate roadway, upgrade guardrail and install rumble strips

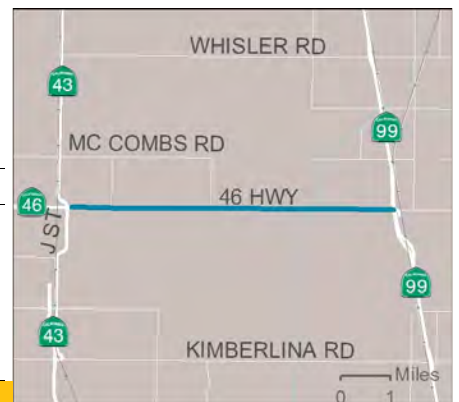

**PROJECT COST:** \$17,500,000 Cost estimates are subject to revision.


**ENV** 100% *Expected completion date March 2024*  
**DES** 5% *Expected start date March 2024*  
**ROW** 5% *Expected start date March 2024*  
**CON** 0% *Expected start date July 2025*

KERSHOPP2206 - 06-1A760 - Project Manager: Shavonne Conley

## PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

### Countywide - Highway Safety and Maintenance

SR 46 - PM 33.2/46 - Near Lost Hills / Wasco - rehabilitate roadway, add maintenance vehicle pull-outs and other improvements

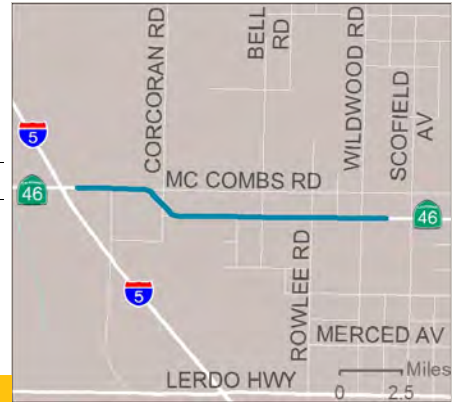

**PROJECT COST:** \$20,000,000 Cost estimates are subject to revision.

**ENV** 50% *Expected completion date August 2024*  
**DES** 0% *Expected start date July 2024*  
**ROW** 0% *Expected start date July 2024*  
**CON** 0% *Expected start date July 2025*

KERSHOPP2204 - 06-1A680 - Project Manager: Shavonne Conley

I-5 - PM R0.0/4.4 - Near Lebec Los Angeles County Line to Lebec Road - rehabilitate northbound roadway, upgrade guardrails and other improvements



**PROJECT COST:** \$25,400,000 Cost estimates are subject to revision.

**ENV** 100% *Completed June 2021*  
**DES** 100% *Completed June 2023*  
**ROW** 100% *Completed June 2023*  
**CON** 0% *Expected start date April 2024*

KERSHOPP2222 - 06-0X330 - Project Manager: Paul Pineda

I-5 - PM 4.4/10.2 - Near Grapevine Fort Tejon Rd to Grapevine Rd - rehabilitate roadway and other safety projects



**PROJECT COST:** \$95,700,000 Cost estimates are subject to revision.

**ENV** 100% *Completed December 2023*  
**DES** 0% *Expected start date February 2024*  
**ROW** 0% *Expected start date February 2024*  
**CON** 0% *Expected start November 2025*

KERSHOPP2211 - 06-0W920 - Project Manager: Manuel Ornelas

I-5 - PM 0.73/1.08 - Near the Grapevine - at the northbound and southbound Tejon Pass Safety Roadside Rest Areas (SRRAs). upgrade water and wastewater systems at SRRAs.



**PROJECT COST:** \$10,200,000 Cost estimates are subject to revision.

**ENV** 95% *Expected completion date April 2024*  
**DES** 0% *Expected start date March 2024*  
**ROW** 0% *Expected start date March 2024*  
**CON** 0% *Expected start date 2025*

KERSHOPP2210 - 06-0X570 - Project Manager: Paul Pineda



## PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

### Countywide - Highway Safety and Maintenance

I-5 - PM 49.7/52.1 - Near Buttonwillow - Stockdale Hwy and SR 58 - construct median cable barrier



**PROJECT COST:** \$4,100,000 Cost estimates are subject to revision.

**ENV** 100% *Completed July 2021*  
**DES** 100% *Completed March 2023*  
**ROW** 100% *Completed March 2023*  
**CON** 30% *Expected completion date May 2024*

KERSHOPP2217 - 06-1A690 - Project Manager: Victor Aldama

I-5 - PM R15.9/30 - SR 99 to Old River Road - rehabilitate roadway and other safety enhancements



**PROJECT COST:** \$35,700,000 Cost estimates are subject to revision.

**ENV** 95% *Expected completion date March 2024*  
**DES** 0% *Expected start date May 2024*  
**ROW** 0% *Expected start date May 2024*  
**CON** 0% *Expected start date December 2025*

KERSHOPP2208 - 06-0W930 - Project Manager: Anourack Kampraseuth

I-5 - PM 10.2/15.9 - Near Grapevine - Grapevine Rd to I-5/SR 99 separation - rehabilitate roadway and other safety improvements




**PROJECT COST:** \$22,400,000 Cost estimates are subject to revision.

**ENV** 100% *Completed July 2022*  
**DES** 100% *Completed November 2023*  
**ROW** 100% *Completed November 2023*  
**CON** 0% *Expected start date September 2024*

KERSHOPP2216 - 06-0U500 - Project Manager: Shavonne Conley

SR 58 - PM R64.4/67.3 - Near Edison Tejon Hwy to General Beale Rd - rehabilitate roadway and other safety improvements

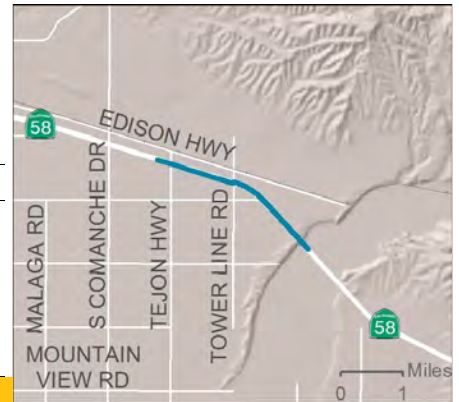

**PROJECT COST:** \$16,100,000 Cost estimates are subject to revision.


**ENV** 100% *Completed January 2022*  
**DES** 100% *Completed March 2023*  
**ROW** 100% *Completed March 2023*  
**CON** 10% *Expected completion date October 2024*

KERSHOPP2219 - 06-0X160 - Project Manager: Victor Aldama

# PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

## Countywide - Highway Safety and Maintenance

SR 58 - PM 77.2/88.56 - Near Tehachapi - Bealville Rd to Broome Rd - rehabilitate roadway and other safety improvements

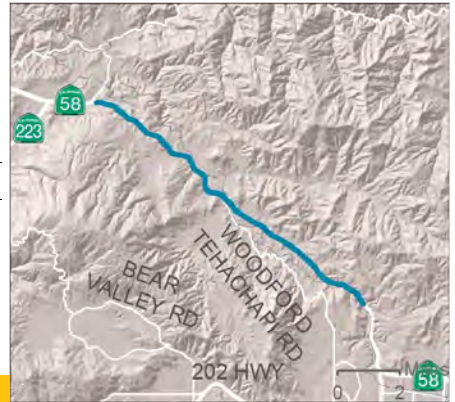


**PROJECT COST:** \$222,700,000 Cost estimates are subject to revision.

- ENV** 100% *Completed 2021*
- DES** 35% *Expected completion date October 2025*
- ROW** 35% *Expected completion date October 2025*
- CON** 0% *Expected start date May 2025*

KERSHOPP2213 - 09-37920 - Project Manager: Jeremy Milos

SR 99 - PM 21.15/24.6 - In Bakersfield - White Lane to California Ave - rehabilitate roadway and other safety improvements

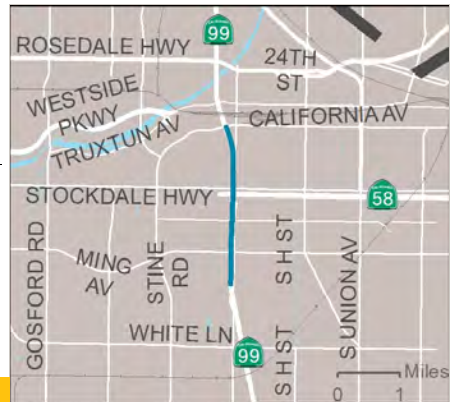


**PROJECT COST:** \$68,300,000 Cost estimates are subject to revision.

- ENV** 100% *Expected completion date January 2024*
- DES** 0% *Expected start date April 2024*
- ROW** 0% *Expected start date April 2024*
- CON** 0% *Expected start date March 2027*

KERSHOPP2212 - 06-0X370 - Project Manager: Shavonne Conley

SR 99 - PM 10.4 / 21.2 - Location In Bakersfield at White Lane OC and Panama Lane OC. - rehabilitate NB lanes and vertical clearance correction

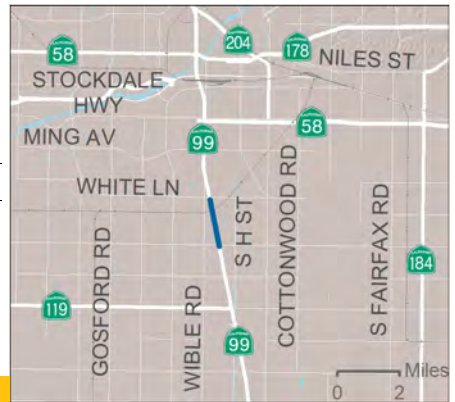


**PROJECT COST:** \$56,000,000 Cost estimates are subject to revision.

- ENV** 100% *Completed March 2018*
- DES** 100% *Completed May 2020*
- ROW** 100% *Completed April 2021*
- CON** 90% *Expected completion February 2024*

KERSHOPP1801 - 06-0Q920 - Project Manager: Paul Pineda

SR 99 - PM 54.6/54.6 - In Delano - remodel and expand existing maintenance station to include ADA improvements

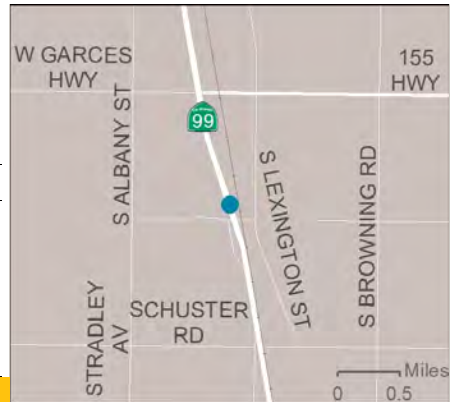

**PROJECT COST:** \$6,800,000 Cost estimates are subject to revision.

- ENV** 100% *Completed July 2023*
- DES** 50% *Expected start date December 2023*
- ROW** 50% *Expected start date December 2023*
- CON** 0% *Expected start date July 2025*


KERSHOPP2203 - 06-1A810 - Project Manager: Shavonne Conley



# PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

## Countywide - Highway Safety and Maintenance

Summary Project Map: Countywide - Highway Safety and Maintenance

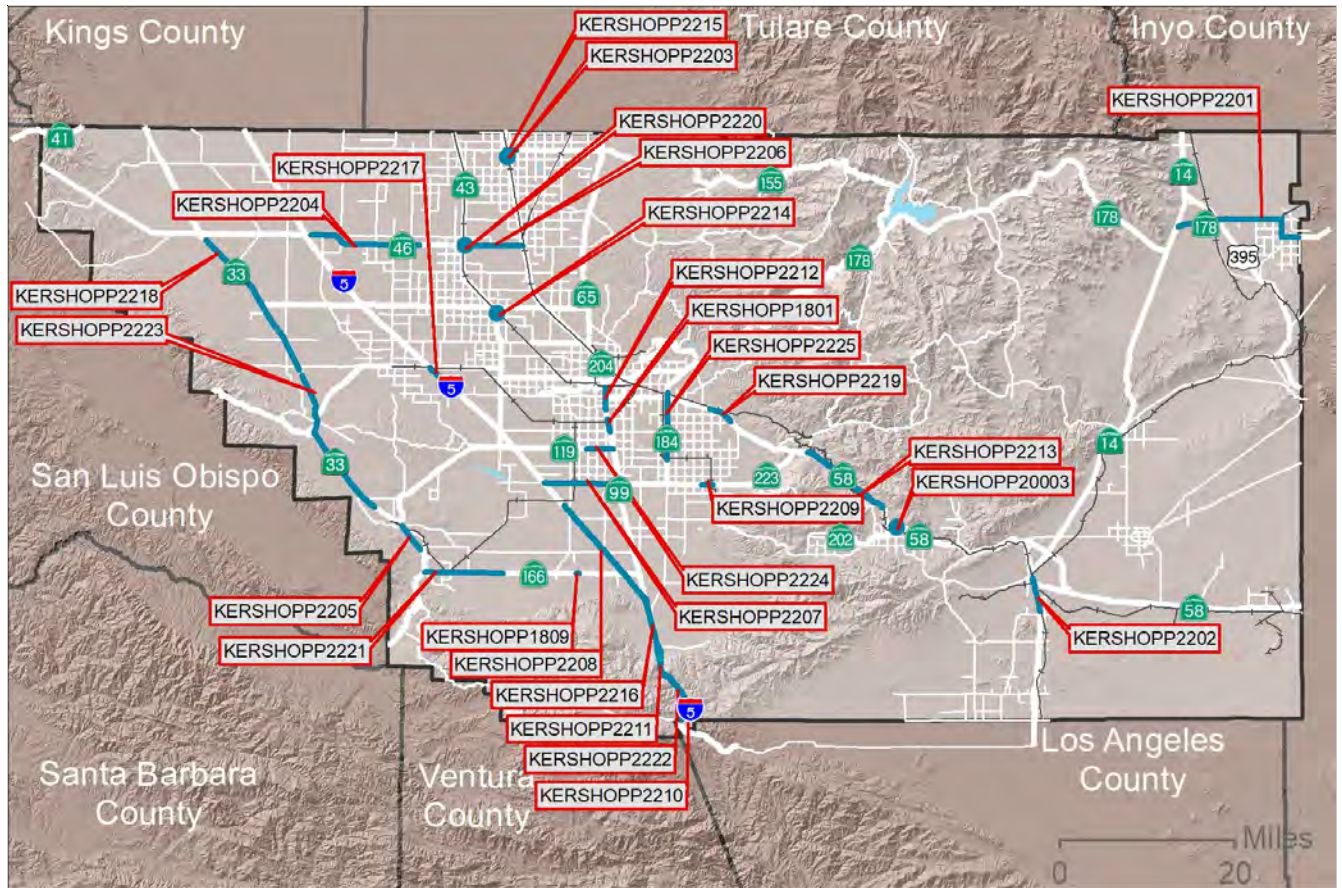

## PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

### Regional Area - Countywide Non-Metro

SR 14 – PM 53.0/58.3 - Freeman Gulch Widening Segment 2 (5.3 miles) - from 4.8 miles south of SR 178 west to 0.5 mile north of SR 178 West - widen to four lanes




**PROJECT COST:** \$48,000,000      Cost estimates are subject to revision.

**ENV**    100%  
**DES**    30%    *Completion date to be determined*  
**ROW**    0%    *Funding not yet determined*  
**CON**    0%    *Funding not yet determined*

KER010103 - EA 06-45712 - Project Manager: Jill Tognazzini

SR 46 - PM 26.4/30.0 - Route 46 Expressway (3.4 miles) - from 1.0 mile w of Brown Material Road to the California Aqueduct - widen to 4 lanes (Segment 4C)

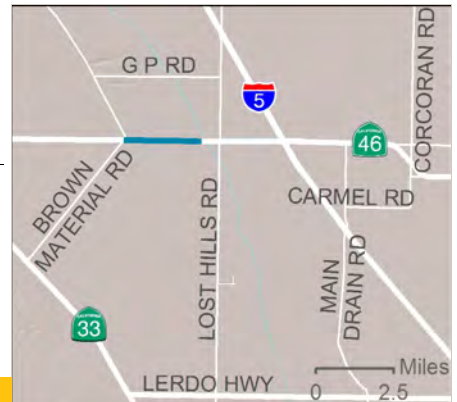

**PROJECT COST:** \$37,000,000      Cost estimates are subject to revision.

**ENV**    100%    *Updates required for project split*  
**DES**    100%    *Completed August 2022*  
**ROW**    100%    *Completed August 2022*  
**CON**    45%    *Expected completion Summer 2024*


KER200101 - 06-44256 - Project Manager: Marlo Carlos



# PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

## Regional Area - Countywide Non-Metro

Summary Project Map: Regional Area - Countywide Non-Metro

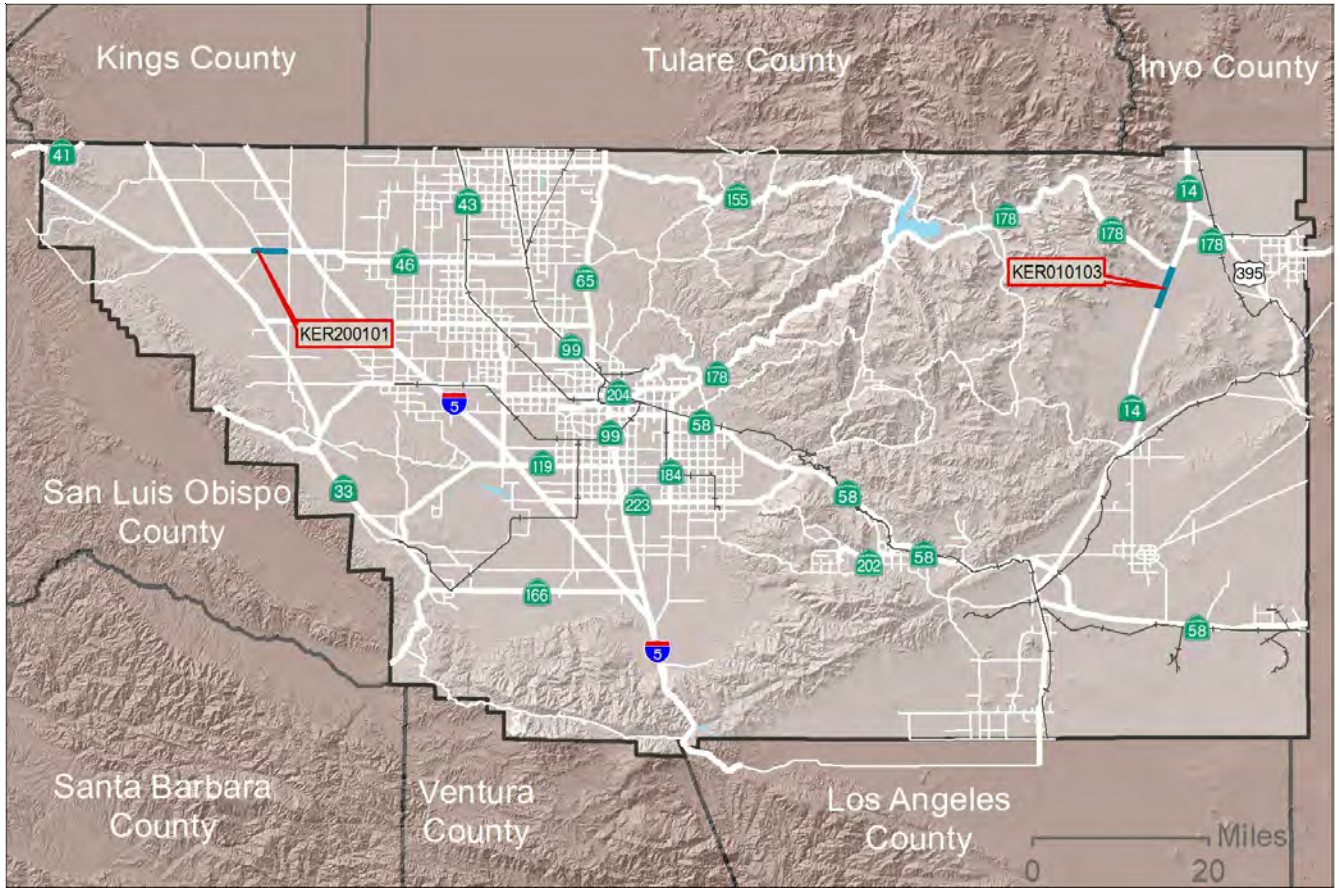




## PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

### Regional Area - Metropolitan Bakersfield - Thomas Road Improvement Program or "TRIP"

Hageman Flyover - extend Hageman Road east to SR 204 / Golden State Avenue.

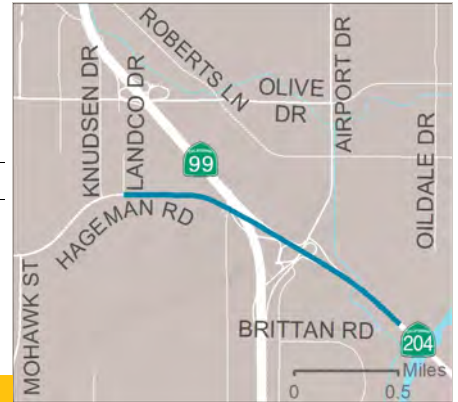


**PROJECT COST:** \$73,000,000 Cost estimates are subject to revision.

**ENV** 100% *Completed*  
**DES** 95% *Completion date to be determined*  
**ROW** 0% *Completion date to be determined*  
**CON** 0% *Start & Completion date to be determined*

KER020604 - EA 06-48450 - Project Manager: Paul Archer

SR 58 - PM T52.1 / R52.5 and SR 99 - PM 21.2 / PM 26.26 - The Bakersfield Freeway Connector Project will construct operational Improvements on SB SR 99 at SR 58 includes auxiliary lanes

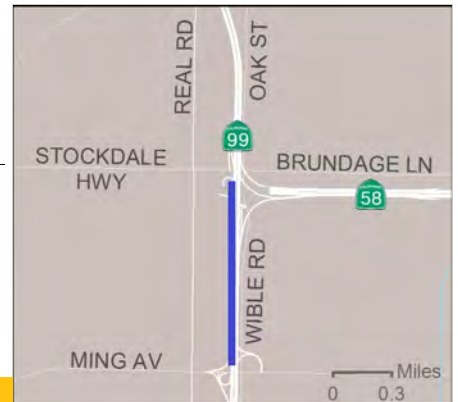

**PROJECT COST:** \$113,000,000 Cost estimates are subject to revision.

**ENV** 100% *Completed*  
**DES** 100% *Completed 2018*  
**ROW** 100% *Completed 2018*  
**CON** 99% *Completion in April 2024*

KER19001 - 06-48466 - Project Manager: Paul Archer

SR 58 - PM T31.7 / R55.6 - Centennial Corridor - Connector from Westside Parkway to SR 58/99 - Construct a new 6-lane freeway on an 8-lane right-of-way



**PROJECT COST:** \$210,800,000 Cost estimates are subject to revision.


**ENV** 100% *Completed January 2016*  
**DES** 100% *Completed December 2018*  
**ROW** 100% *Completed November 2018*  
**CON** 99% *Completion in April 2024*

KER080109 - EA 06-48460 - Project Manager: Paul Archer

# PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

## Regional Area - Metropolitan Bakersfield - Thomas Road Improvement Program or "TRIP"

### Summary Project Map: Regional Area - Metropolitan Bakersfield - Thomas Road Improvement Program or "TRIP"

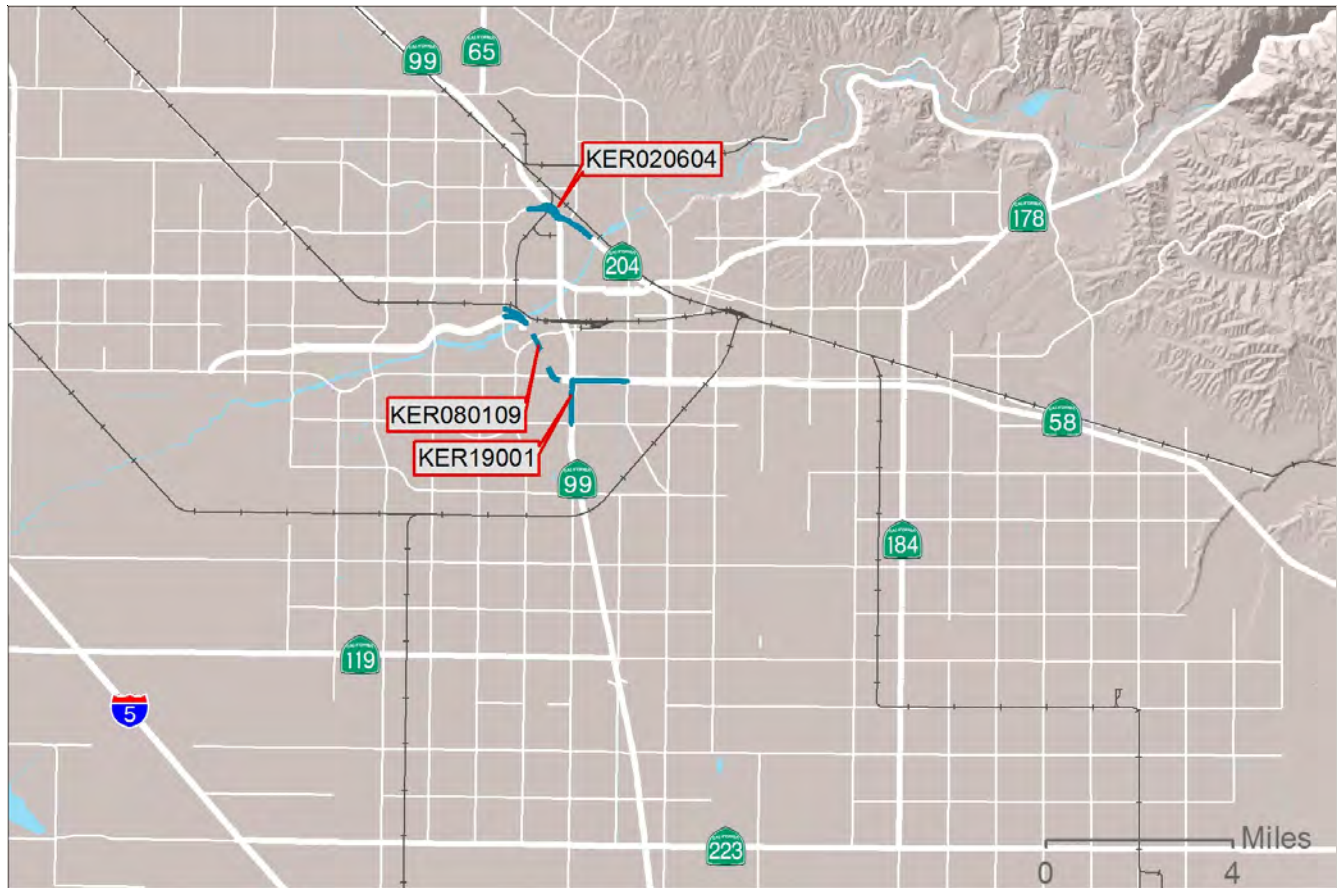

# PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

## Highway Projects Completed in Last Two Years

SR 14 - PM 4.7 /12.60 - Rosamond & Mojave area - rehabilitate roadway




**PROJECT COST:** \$73,615,000 Cost estimates are subject to revision.

- ENV** 100% *Completed June 2018*
- DES** 100% *Completed January 2020*
- ROW** 100% *Completed January 2020*
- CON** 100% *Completed December 2022*

KERSHOPP20001 - 09-36740 - Project Manager: Jill Tognazzini

SR 46 - PM 29.7/31.9 - Route 46 Expressway (2.2 miles) - from 0.2 miles west of California Aqueduct Bridge to 1.4 miles east of Lost Hills Road - widen to 4 lanes (Segment 4B)

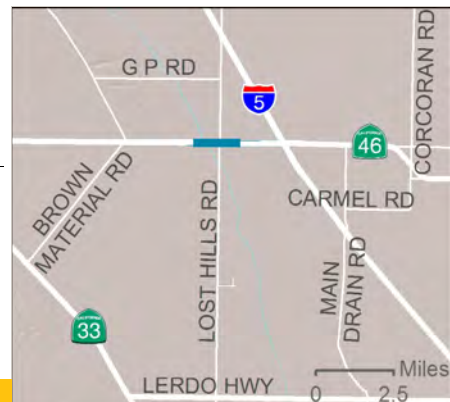


**PROJECT COST:** \$39,903,000 Cost estimates are subject to revision.

- ENV** 100%
- DES** 100% *Completed July 2020*
- ROW** 100% *Completed July 2020*
- CON** 100% *Completed November 2023*

KER120108 - 06-44255 - Project Manager: Marlo Carlos

SR 99 - PM 24.1 / 28.4 - Bakersfield - Palm Avenue Overcrossing to Beardsley Canal - Roadway Rehabilitation

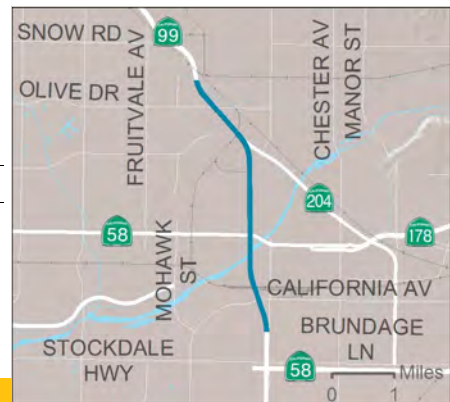

**PROJECT COST:** \$86,000,000 Cost estimates are subject to revision.

- ENV** 100% *Completed August 2016*
- DES** 100% *Completed May 2018*
- ROW** 100% *Completed May 2018*
- CON** 100% *Completed November 2022*

KERSHOPP1432 - 06-0Q280\_ - Project Manager: Paul Pineda

SR 14 - PM 46.2/53 - Near Armistead Red Rock Canyon Rd to SR 178 - rehabilitation roadway



**PROJECT COST:** \$8,700,000 Cost estimates are subject to revision.

- ENV** 100% *Completed June 2021*
- DES** 100% *Completed August 2022*
- ROW** 100% *Completed June 2022*
- CON** 100% *Completed August 2023*

KERSHOPP2227 - 09-37890 - Project Manager: Jill Tognazzini



# PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

## Highway Projects Completed in Last Two Years

SR 184 - PM L0.9/L1.1 - near Weedpatch from 0.1 mi south to 0.1 mi - Intersection Improvements: construct roundabout



**PROJECT COST:** \$3,600,000 Cost estimates are subject to revision.

- ENV** 100% *Completed September 2018*
- DES** 100% *Completed June 2021*
- ROW** 100% *Completed June 2022*
- CON** 100% *Expected completion January 2024*

KERSHOPP1806 - 06-0V280 - Project Manager: Paul Pineda

SR 202 - PM 4.70/5.10 - Near Tehachapi at Cummings Valley Road - construct intersection improvements including new turn pocket




**PROJECT COST:** \$5,044,000 Cost estimates are subject to revision.

- ENV** 100% *Completed June 2019*
- DES** 100% *Completed September 2021*
- ROW** 100% *Completed September 2022*
- CON** 100% *Completed May 2023*

KERSHOPP20002 - 09-36720 - Project Manager: Jill Tognazzini

SR 223 - PM 21.0 / 21.3 - In and Near Arvin, at Derby Street - Install traffic signals

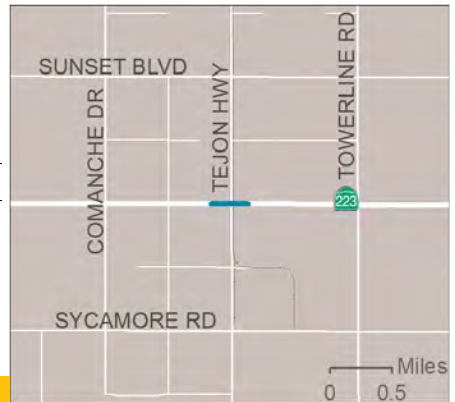

**PROJECT COST:** \$2,603,000 Cost estimates are subject to revision.


- ENV** 100% *Completed August 2015*
- DES** 100% *Completed August 2020*
- ROW** 100% *Completed September 2020*
- CON** 100% *Completed May 2022*

KERSHOPP120202B - 06-0S510 - Project Manager: Paul Pineda

# PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE

## Highway Projects Completed in Last Two Years

Summary Project Map: Highway Projects Completed in Last Two Years

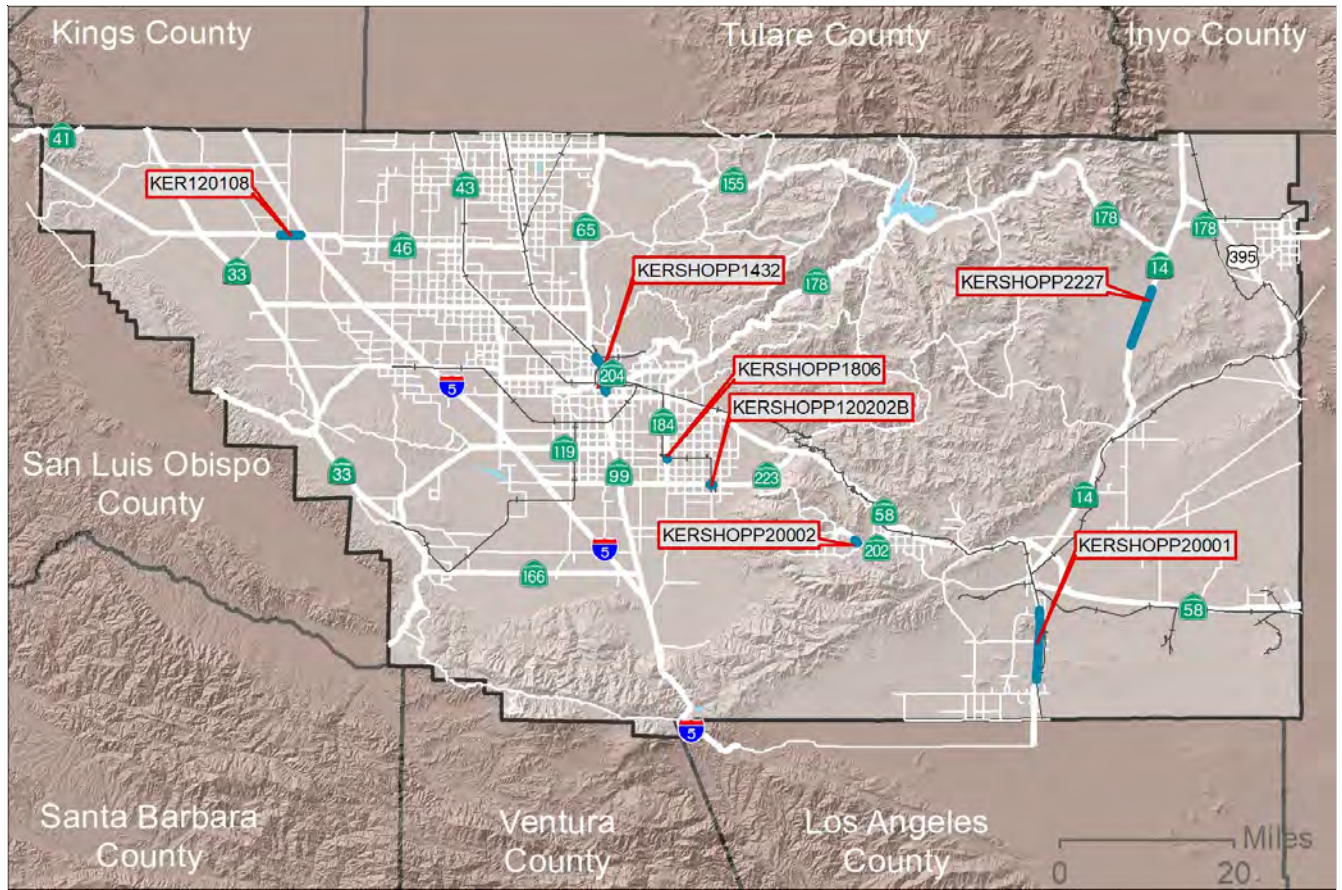





CENTENNIAL MAINLINE | LOOKING WEST AT THE NEW REAL ROAD UNDER CROSSINGS: FROM LEFT TO RIGHT THESE BRIDGES ARE (1) EASTBOUND 58 TO MING AVENUE OFF-RAMP, (2) EASTBOUND 58 TO SOUTHBOUND 99 CONNECTOR RAMP, (3) 58 EAST AND WEST MAINLINE FREEWAY, AND (4) NORTHBOUND 99 TO WESTBOUND 58 CONNECTOR RAMP. SEPTEMBER 2022



**Centennial Mainline  
SR58/99 Interchange  
Looking NW to various  
connector ramps in progress  
April 2022**

**Centennial Mainline  
California Avenue undercrossing  
looking north  
September 2021**



**Centennial Mainline Real Road  
Bridges to various connector  
ramps. Looking east towards  
SR 99 & SR 58  
September 2021**



**This progress report** is updated and distributed to the Kern Council of Governments Board of Directors and the general public, on a quarterly basis. The listed projects are funded through a combination of local, state and federal transportation programs.

**These projects** add new lanes to existing highways, construct new roadways and maintain or improve existing roadways or related infrastructure. Cost estimates provided in the following pages include costs for construction, rights-of-way, design and support costs.

**This report** may be downloaded by visiting Kern COG's website at: [www.kerncog.org](http://www.kerncog.org). The report link is located towards the bottom of the home page under the "Projects of Regional Significance" section.

